IT Project Management

AI Acknowledgment

This report was developed by the student. AI tools such as ChatGPT and Gemini LLM were used to assist with research organization and idea generation. Grammarly was used for proofreading and grammar correction. All data, interpretations, writing, and conclusions are original.

Table of Contents

1. Introduction and Project Overview

1.1 Background of the Project

1.2 Project Aim and Scope

1.3 Chosen SDLC: Agile (Scrum)

2. Task 1: Project Initiation and Planning

2.1 Project Objectives (SMART Framework)

2.2 Stakeholder Identification and Roles

3. Task 2: Project Scheduling and Risk Management

3.1 Project Schedule and SDLC Model

3.2 Risk Register and Mitigation

4. Task 3: Testing and Quality Assurance

4.1 Testing Strategy

4.2 Quality Assurance (ISO 25010)

5. Task 4: Agile Prioritization and Estimation

5.1 MoSCoW Prioritization

5.2 Estimation Approach

6. Task 5: Reporting, Monitoring, and Control

6.1 Project Progress Report

6.2 Monitoring and Tracking (Burn Down Chart)

7. Conclusion

8. References

9. Appendices

Appendix A – Gantt Chart

Appendix B – Risk Register

Appendix C – Progress Report Template

Appendix D – Burn Down Chart

1. Introduction and Project Overview

1.1 Background of the Project

In the field of commerce, e-commerce is a fast-growing sector. In general, the idea of business focuses on the happiness and satisfaction of the consumer. A successful and competitive business is shaped by these two key elements. Thousands of customer queries are answered daily by XYZ, which is an e-commerce platform that is growing quickly. For level 1 assistance, the company intends to deploy an AI chatbot that can answer Frequently Asked Questions through the company's official website and mobile application. The management aims to lower operating expenses, speed up response times, reduce the workload for human agents, and improve customer satisfaction by approving this project.

1.2 Project Aim and Scope

The aim of this project is to develop and deploy an AI chatbot for level 1 support, capable of handling frequently asked questions through the company website and mobile application to reduce the operational costs, improve response time, reduce the workload on human agents, and increase customer satisfaction and happiness. The process of this project involves Chatbot training, the integration of the chatbot in the e-commerce system, testing, and post-deployment evaluation.

1.3 Chosen SDLC: Agile (Scrum)

The chosen Software Development Life Cycle for this project is Agile (Scrum). According to NCC education (2025), “Agile software development is a methodology focused on iterative development, where requirements and solutions evolve through collaboration between self-organizing cross-functional teams. It prioritizes adaptive planning, evolutionary development, early delivery, and continual improvement, aiming to deliver small, incremental releases frequently”. The Scrum agile method, on the other hand, is an incremental, time-boxed framework for an agile development process. In Scrum, a time-box is a set amount of time given for a particular event, activity, or event (sprint). Scrum's primary focus is on project and team management. Teams, jobs, events, artifacts, and rules are the main factors shaping this system. The Product Owner plays a crucial role in Scrum, establishing and prioritizing the product backlog, speaking for the customer, and making sure the development team provides stakeholders with the highest level of value possible. Furthermore, the Scrum Master is a servant leader and facilitator. The Scrum Master is responsible for making sure the Scrum team follows the Scrum framework, reducing obstacles, and promoting a cooperative and self-organizing environment. (NCC education, 2025)

This model has several advantages that can positively impact the overall development of this project. The benefits of this model are as follows:

1. Flexible. Allowing continuous changes to the plans as needed
2. It promotes the concept of teamwork. Allowing the team to work closely together on a certain project from start to finish.
3. It allows for consistent improvement as the project can receive continuous feedback. (NCC education, 2025)

2. Task 1: Project Initiation and Planning

2.1 Project Objectives (SMART Framework)

The objectives of this project include:

1. Developing and deploying a multilingual AI Chatbot capable of handling more than 70% of customer queries efficiently within the range of 6 months
2. Reducing the operational cost by decreasing the percentage of customers needing human customer support to less than 30% within the range of 3 months after deployment. Allowing for minimal human workload and leaving human agents for more complex problems
3. Integrating the AI Chatbot in the company's official website and mobile application within a range of 4 months
4. Achieving an increased percentage of customer satisfaction to at least 80% within 2 months after deployment by initiating surveys after a few months of the AI Chatbot's launch
5. Training the support team to effectively manage and monitor the Chatbot model within the first two weeks of launching

These objectives follow the SMART criteria. Which refers to Specific, Measurable, Achievable, Relevant, and Time-bound. Allowing for continuous monitoring and management (Aldridge and Colvin, 2024)

The alignment of the provided objectives to the SMART criteria is as follows:

1. Specific: The main aim and objective of this project is to implement an AI chatbot to reduce operational costs, increase customer satisfaction, and reduce human workload
2. Measurable: Targeting a certain percentage for each objective that is achievable within a proposed time. For example, the chatbot's purpose is to handle at least 70% of customer queries, reduce the human workload and operational cost to a minimum 30%, and achieve a high rating of customer satisfaction to reach at least 80%. All of which are expected to happen within the range of 6 months. According to KumoHQ (2025), “Advanced [Chatbots] solutions need up to six months”, which explains exactly why the range of 6 months was chosen to develop the AI Chatbot.
3. Achievable: the project development heavily relies on its main aim, which is to develop an AI Chatbot within a specific time and with clearly defined objectives to achieve the goal of the project.
4. Relevant: the development process of the project is clearly aligned with the management goal.
5. Time-bound: the project timeline is clearly defined. Being completed within the range of 6 months to help the management identify the possible completion date.

(Aldridge and Colvin, 2024) (NCC education, 2025)

2.2 Stakeholder Identification and Roles

According to NCC education (2025), “ Stakeholders are those with an interest in [the] project’s outcome.” Stakeholders can be “Members of a project team, project managers, executives, project sponsors, customers, and users.” (NCC education, 2025)

Additionally, Stakeholders, in specific terms, are “ People who will be affected by [the] project at any point in its life cycle, and their input can directly impact the outcome” (NCC education, 2025). Furthermore, key project stakeholders are those with the power and influence to determine whether or not a project succeeds. (NCC education, 2025).

Stakeholders are divided into 2 categories: External stakeholders and internal stakeholders.

External stakeholders consist of:

1. Customers
2. Government
3. Contractors
4. Suppliers

While Internal stakeholders consist of:

1. Project manager
2. Project sponsor
3. Steering committee
4. Executives
5. Resource manager (NCC education, 2025)

For this project, the main stakeholders are identified as follows:

1. Project sponsor
2. Product owner
3. Scrum master
4. Development team
5. Customer

The project sponsor functions as a pivotal internal stakeholder who's been clearly identified and holds governance responsibilities over the entire project while simultaneously providing strategic direction plus management oversight (NCC education, 2025). Meanwhile the product owner carries the burden of guaranteeing that development teams are delivering maximum value to all stakeholders involved, this individual essentially becomes the customer's representative voice and takes charge of both defining as well as prioritizing what goes into the product backlog.

When backlog items gets reviewed, the product owner ensures their continued relevance through a comprehensive process. Outdated user stories are systematically removed from consideration, new user stories gets created whenever necessary, each story's relative importance undergoes reconsideration, and previously unassessed stories receives estimation while recalculations occurs based on emerging data (NCC education, 2025). The scrum master, on the other hand operates as both facilitator and what's termed a servant leader - their primary responsibility involves ensuring the Scrum team's adherence to established Scrum framework principles and practices throughout.

This process involves offering team members direction, support, and advice to make sure they are aware of their duties and responsibilities. (NCC education, 2025). He/she is also in charge of reducing obstacles, creating a cooperative and self-organizing environment, developing a positive team culture, supporting professional growth, and enabling team communication, cooperation, and task coordination. They also manage workloads, prioritize tasks, keep an eye on individual and team performance, and make sure deadlines are reached. (NCC education, 2025)

The development team forms a crucial part of the stakeholder management. The development team is in charge of creating the program (Which is the AI Chatbot in the case of this project). During the Construction (Coding or Development) stage, they use the system design and specification as input. The product owner guarantees that they provide stakeholders with the most value possible.

Various developers are given tasks that are divided into units or modules. Additionally, in order to determine the tasks for the next sprint, the team attends a meeting. They also participate in brainstorming sessions to find task-related assumptions. (NCC education, 2025).

By using agile methods like Planning Poker and T-shirt sizing, the Development Team is also highly involved with project estimation. Engineers, managers, and stakeholders must come to an agreement on estimation. Additionally, Unit testing, which involves testing individual parts or code units, is another responsibility of developers.

When utilizing Extreme Programming, developers use Pair Programming, which involves two programmers working side by side while simultaneously coding and auditing. (NCC education, 2025)

Finally, the most important part of stakeholder management is the customer. The customer factor being involved is what makes the project successful. And the lack of customers being involved in the development process leads to the project's failure. (NCC education, 2025)

Customers are a key element in the requirements analysis and specifications phase, and methods for gathering requirements include interviewing system users, conducting surveys, and presenting prototypes. (NCC education, 2025)

The Customer factor plays a crucial role in the product initiation procedure. Before the program is put into use, users test it to find issues that developers might have missed. This procedure is called user acceptance testing. Which involves end users (customers) confirming that the software satisfies their needs and performs as intended before the final deployment. (NCC education, 2025)

In Agile, the team collaborates closely with the customer to get their opinions. In Extreme Programming, the customer defines the tests and sits with the team every day to conduct them. (NCC education, 2025)

3. Task 2: Project Scheduling and Risk Management

3.1 Project Schedule and SDLC Model

The main model used to develop this project is Agile (Scrum). As “It prioritizes adaptive planning, evolutionary development, early delivery, and continual improvement, aiming to deliver small, incremental releases frequently.” (NCC education, 2025), it also has considerable advantages such as flexibility, teamwork support, and continuous improvements and feedback.

The project plan contains different phases. Each phase consists of tasks that are divided throughout the time range assigned (which is 6 months). The project phases include:

1. Planning and initiating the project
2. Gathering and analysing the data
3. Designing the system (Chatbot)
4. The development process
5. Testing phase
6. Deployment phase and training the team
7. Post-deployment phase

Each task has an estimated duration during which it can be completed. For the planning and project initiation phase, it is estimated to take action during the first 2-3 weeks of month 1. The data gathering and analysis phase is expected to be completed during the last week of month 1 until the beginning of month 2. Additionally, the Chatbot designing phase would be completed in the final week of month 2 until the beginning of month 3.

Moreover, the development process, which consists of training the model and integrating it into the company's database including the frequently asked questions module, and linking the chatbot with the website and mobile application. Is estimated to finish in month 4. The testing phase would be completed in month 5. Furthermore, the deployment phase which also includes training the support team would finish in month 6. Lastly, the post-deployment phase comes later in month 6.

The Gantt chart for this project will be provided in Appendix A

3.2 Risk Register and Mitigation

During the development of the project, delays and issues are expected to occur, and it's important to bear in mind these risks and assess them properly. Key potential risks could include:

1. Data breach occurring during chatbot training due to how customer data gets handled
2. Failing to integrate the chatbot with website or mobile app leading to immediate stop
3. Inaccurate natural language processing responses that leads to poor user satisfaction
4. Incomplete training data which limits chatbot performance capabilities
5. Vendor delay or SaaS dependency issues that impacts schedule
6. Too many new ideas that causes delays leading to missing the deadline
7. Lack of proper skills in team members in AI and natural language processing technologies
8. Unexpected increase on the budget due to underestimating the cost of development and integration
9. Cybersecurity threats
10. User adoption rates decrease if customers prefer human support.

Each risk is equipped with the level of likelihood of the risk happening during the development of the project.

Risk identification and assessment play an important role in project success. Dealing properly with the potential risk that could happen during the development of a project eliminates potential wasted expenses. Which can be taken a good use of in other aspects of project development. Key risk assessment practices are as follows:

1. Implement data encryption method to avoid potential data breaches, follow GDPR Compliance, and restrict access to authorised people only. (GDPR.eu, 2018)
2. Perform early system testing to identify issues and backup servers
3. Constant model training on real data and chat logs
4. Expanding the model training on the company database and the open source frequently asked questions module
5. Put strict and clear delivery rules in terms of vendors and potential delays
6. Stick to the project plan and prioritize key features to implement to avoid wasted expenses
7. Conduct training sessions, courses, and workshops for team members to get familiarized with the chatbot
8. Taking control of the budget by revising the spending to avoid wasted expenses
9. Use authentications and internet protocols and implement CAPTCHA and perform regular check ups for potential vulnerabilities.
10. Provide hybrid support to customers which consists of a human agent and an AI agent and initiate educational courses and campaigns for the customers to increase the chance of acceptance.

The risk register table will be provided in Appendix B

4. Task 3: Testing and Quality Assurance

4.1 Testing Strategy

The project follows four key testing strategies. Which are:

1. unit testing
2. integration testing
3. user acceptance testing
4. performance testing.

Each testing strategy forms and shapes a crucial part of the project.

Unit testing is a testing strategy that involves “testing individual components or units of [the chatbot] to ensure [it] functions correctly in isolation.” (NCC education, 2025). In the unit testing strategy. The System gets chosen and tested accordingly. (NCC education, 2025) This step is crucial as it ensures every element of the chatbot is functioning properly as designed before the integration happens.

Additionally, Integration testing is “a software-testing approach in which various application components or modules are joined and tested to evaluate how well they work together. Integration testing seeks to help ensure that these assembled parts can communicate with each other and interact successfully.” This step helps in assessing how the natural language processing engine of the chatbot interacts with the company's e-commerce databases to make sure that the data flows seamlessly between both systems. (IBM, no date)

Moreover, “User acceptance testing (UAT), also called application testing or end-user testing, is a phase of software development in which the software is tested in the real world by its intended audience. UAT is often the last phase of the software testing process and is performed before the tested software is released to its intended market. The goal of UAT is to ensure software can handle real-world tasks and perform up to development specifications” (TechTarget, no date). This strategy makes sure that the final version of the chatbot meets the expectations of the user.

Finally, “Performance Testing is a type of software testing that ensures software applications perform properly under their expected workload. It is a testing technique carried out to determine system performance in terms of sensitivity, reactivity, and stability under a particular workload.” (GeeksforGeeks, 2025)

This type of testing evaluates the system performance and scalability (GeeksforGeeks, 2025)

This testing strategy is essential ahead of Chatbot deployment because it allows for determining the chatbot's performance and solving potential problems before the official system launch.

4.2 Quality Assurance (ISO 25010)

To guarantee customer satisfaction and the success of any digital product, software quality is important. The ISO 25010 standard is significant because it provides a model for assessing and enhancing software quality. (Souza, 2025)

According to Britton (2021), ISO 25010 is “a software quality standard. It describes the models, consisting of characteristics and sub-characteristics, for both software product quality, and software quality in use together with practical guidance on the use of the quality models.”

Key characteristics of ISO 25010 standard are:

1. Functional suitability: refers to the ability of a system or product to fulfil both public and private demands
2. Reliability: refers to the ability of a system, product, or component to carry out certain tasks under specific conditions.
3. Performance efficiency: refers to the performance in relation to the quantity of resources utilised.
4. Usability: refers to the degree to which a system or product may be utilised to successfully, efficiently, and satisfactorily accomplish specific goals.
5. Security: refers to the degree to which a system or product protects data and information against vulnerabilities in security. (Britton, 2021)

The AI Chatbot adheres to ISO 25010 for software quality to ensure that it meets the expectations of the customers and the business. In terms of functional suitability, it can be achieved by dedicating the features of the chatbot according to the company's goals. Additionally, reliability can be achieved by backing up systems and constant monitoring to make sure that the servers are stable most of the time. Moreover, performance efficiency can be evaluated by conducting intensive testing on the system, such as high loading to make sure that the chatbot can provide reliable and fast responses in peak times. Furthermore, the usability can be improved by conducting surveys to gather the feedback of the customers to find out how happy customers are when using the chatbot. Finally, data can be secured by implementing encryption models, authentication, and regular vulnerability checkups.

5. Task 4: Agile Prioritization and Estimation

5.1 MoSCoW Prioritization

Since the project follows the Agile (Scrum) model, the MoSCow method plays a key role in prioritizing certain project tasks.

> According to ProductPlan (2025), the MoSCow method is" a popular prioritization technique for managing requirements. The acronym MoSCoW represents four categories of initiatives: must-have, should-have, could-have, and won't-have, or will not have right now. Some companies also use the "W" in MoSCoW to mean "wish."

Initiatives that are considered musts for the team fall under the (must have) category. They stand for unquestionable requirements for the project, product, or release in question. (ProductPlan, 2025). For the AI chatbot project, there are features in which the chatbot cannot properly function without them being exist. Which are considered very important for the first sprint such as developing the core natural language processing, building the basic frequently asked questions database for regular and common customer queries, and connecting the databases of the company along with the first version of the chatbot interface. These elements are very important to follow in order to demonstrate a working product before the end of the first sprint

In addition, Initiatives that are only a step below must haves are called should haves. They are not crucial, but they are necessary for the project, product, or release. The project or product still works even if it is excluded. (ProductPlan, 2025). For example, one of the tasks that is considered should have for the project in the first sprint could be

having the chatbot support two essential languages such as Arabic and English. Additionally, could have category have less impact on the project outcome as the essential functionality of the product (chatbot) does not need could have initiatives. (ProductPlan, 2025). For example, adding voice interaction features and creating custom chatbot themes fall under the could have category. They can be included if only the major tasks in the first sprint are completed as the chatbot can still function well without them being exist.

Finally, the will not have category involves postponing specific features to another timeframe. Which can be decided by the development team as they can manage the project expectations with the help of this category. (ProductPlan, 2025). Features that could fall under this category in terms of the chatbot project perspective could include adding an analytics dashboard to track performance and integrating social media messaging and interactions. With the help of this category, the development team can manage what should be included and what should not be for the meantime to avoid any potential delay and focus on more critical aspects of the project.

5.2 Estimation Approach

For this project, since it follows a range of 6 months timeline, there are key elements that require proper estimation. These key elements are as follows:

1. Gathering and analysing the data
2. Designing the system (Chatbot)
3. The development process
4. Testing phase
5. Deployment phase and training the team

Each element can impact the project overall. Including scheduling, costs, and sprint. Therefore, the chosen estimation approach for this project is the planning poker technique as it is suitable with the project model (Agile Scrum). It also allows for engaging and fun collaboration with stakeholders such as the product owner, scrum master, and the development team by using story points. It also supports continuous adjustments, especially when training the chatbot. This approach is also known for its flexibility. Making it the most suitable choice for this project to make sure that the forecasting is accurate most of the time. (Cohn, 2025)

6. Task 5: Reporting, Monitoring, and Control

6.1 Project Progress Report

Drawing a progress report helps in summarizing what has been done throughout the project. Particularly in a specific phase. According to the project gantt chart that outlines the timeframe and task that should be carried out throughout the project. The first phase of the project is planning and initiating the project. Which is estimated to take action during the first 2- weeks of month 1.

The project report contains 6 major elements that summarizes the working of the project. These elements are as follows:

1. Completed activities
2. Activities in progress
3. Risks
4. Risk assessment
5. Current phase
6. Next steps

Each element represents different activities taken throughout the project initiation phase. Especially in first 2-3 weeks.

Key activities mentioned involves project kick off meeting, project outline, defining objectives, and identifying stakeholders. These activities can help in shaping the project. Other key activities include identifying risks such as potential delivery delay and confirming delivery rules with vendors as a risk assessment. Finally, identifying next

steps forms a major part of the project. Key activities mentioned include finalizing the project initiation phase and planning for the next phase, which is data gathering and analysis.

The project report template will be provided in Appendix C

6.2 Monitoring and Tracking (Burn Down Chart)

The burndown chart allows for tracking the progress. For this project. The burn down chart was created for the first phase. Which is named Planning and initiating the project. The burn down chart includes key elements such as sprint day, ideal work remaining (story points), and actual work remaining (story points). Other mentioned elements involve calculating total story points, days in sprint, and story points to complete per day. This burn down chart is perfectly aligned with the project schedule. The burn down chart also reflects that the project is currently ahead of schedule for this phase. For example, on sprint day 10, the ideal remaining work was approximately 32 points but the actual work remaining was only 28 points. This leads that the team is progressing faster than planned.

The burn down chart will be provided in Appendix D

7. Conclusion

In summary, the project outlines the implementation of an AI Chatbot for XYZ E-commerce. The project covers elements such as identifying the aim of the project, stakeholders, the methods used to develop the project, identifying risks and assessing them, developing project schedule (Gantt chart), and constant monitoring of the progress by creating a project report and a burn down chart to actively track progress. By adhering to the development process and methods proposed. The implementation of the AI Chatbot will achieve remarkable success, helping the company in reducing costs, saving critical time for human agents to focus more on complex tasks, and achieving higher levels of customer satisfaction.

8. References

NCC education. (2025). *IT Project Management Topic 3: Project Planning*. [PowerPoint presentation distributed in]. IT Project Management. NCC education.

NCC education. (2025). *IT Project Management Topic 1: Introduction to ITPM*. [PowerPoint presentation distributed in]. IT Project Management. NCC education.

KumoHQ. (2025) *AI Chatbot Development Cost In 2025: Pricing & Key Factors*. Available at: https://www.kumohq.co/blog/ai-chatbot-development-cost (Accessed: 3 November 2025).

Aldridge, C.A. and Colvin, M.E., 2024. Writing SMART objectives for natural resource and environmental management. Ecological Solutions and Evidence, 5(1), p.e12313.

NCC education. (2025). *Business IT Project Topic 1: Introduction to BITP*. [PowerPoint presentation distributed in]. Business IT Project. NCC education.

NCC education. (2025). *IT Project Management Topic 10: Project Organisation*. [PowerPoint presentation distributed in]. IT Project Management. NCC education.

NCC education. (2025). *IT Project Management Topic 4: Project Planning 2*. [PowerPoint presentation distributed in]. IT Project Management. NCC education.

NCC education. (2025). *IT Project Management Topic 2: Stages in Project*. [PowerPoint presentation distributed in]. IT Project Management. NCC education.

NCC education. (2025). *IT Project Management Topic 5: Estimation*. [PowerPoint presentation distributed in]. IT Project Management. NCC education.

NCC education. (2025). *IT Project Management Topic 8: Quality*. [PowerPoint presentation distributed in]. IT Project Management. NCC education.

GDPR.eu. (2018) *General Data Protection Regulation (GDPR) Compliance Guidelines*. Available at: https://gdpr.eu/ (Accessed: 4 November 2025).

IBM. (no date) *What is CAPTCHA?* Available at: https://www.ibm.com/think/topics/captcha (Accessed: 4 November 2025).

IBM. (no date) *What is Integration Testing?* Available at: https://www.ibm.com/think/topics/integration-testing (Accessed: 6 November 2025).

TechTarget. (no date) *User acceptance testing (UAT)*. Available at: https://www.techtarget.com/searchsoftwarequality/definition/user-acceptance-testing-UAT (Accessed: 6 November 2025).

GeeksforGeeks. (2025) *Performance Testing - Software Testing*. Available at: https://www.geeksforgeeks.org/software-testing/performance-testing-software-testing/ (Accessed: 6 November 2025).

Souza, R. (2025) *ISO 25010 Software Quality: An Essential Guide*, 10 March [LinkedIn]. Available at: https://www.linkedin.com/pulse/iso-25010-software-quality-essential-guide-roberta-souza-ibnqe (Accessed: 6 November 2025).

Britton, J. (2021) *What Is ISO 25010?*. Available at: https://www.perforce.com/blog/qac/what-is-iso-25010 (Accessed: 6 November 2025).

ProductPlan. (2025) *What is MoSCoW Prioritization?*. Available at: https://www.productplan.com/glossary/moscow-prioritization/ (Accessed: 6 November 2025).

Cohn, M. (2025) *Planning Poker: An Agile Estimating and Planning Technique*. Available at: https://www.mountaingoatsoftware.com/agile/planning-poker (Accessed: 7 November 2025).

9. Appendices

Appendix A – Gantt Chart

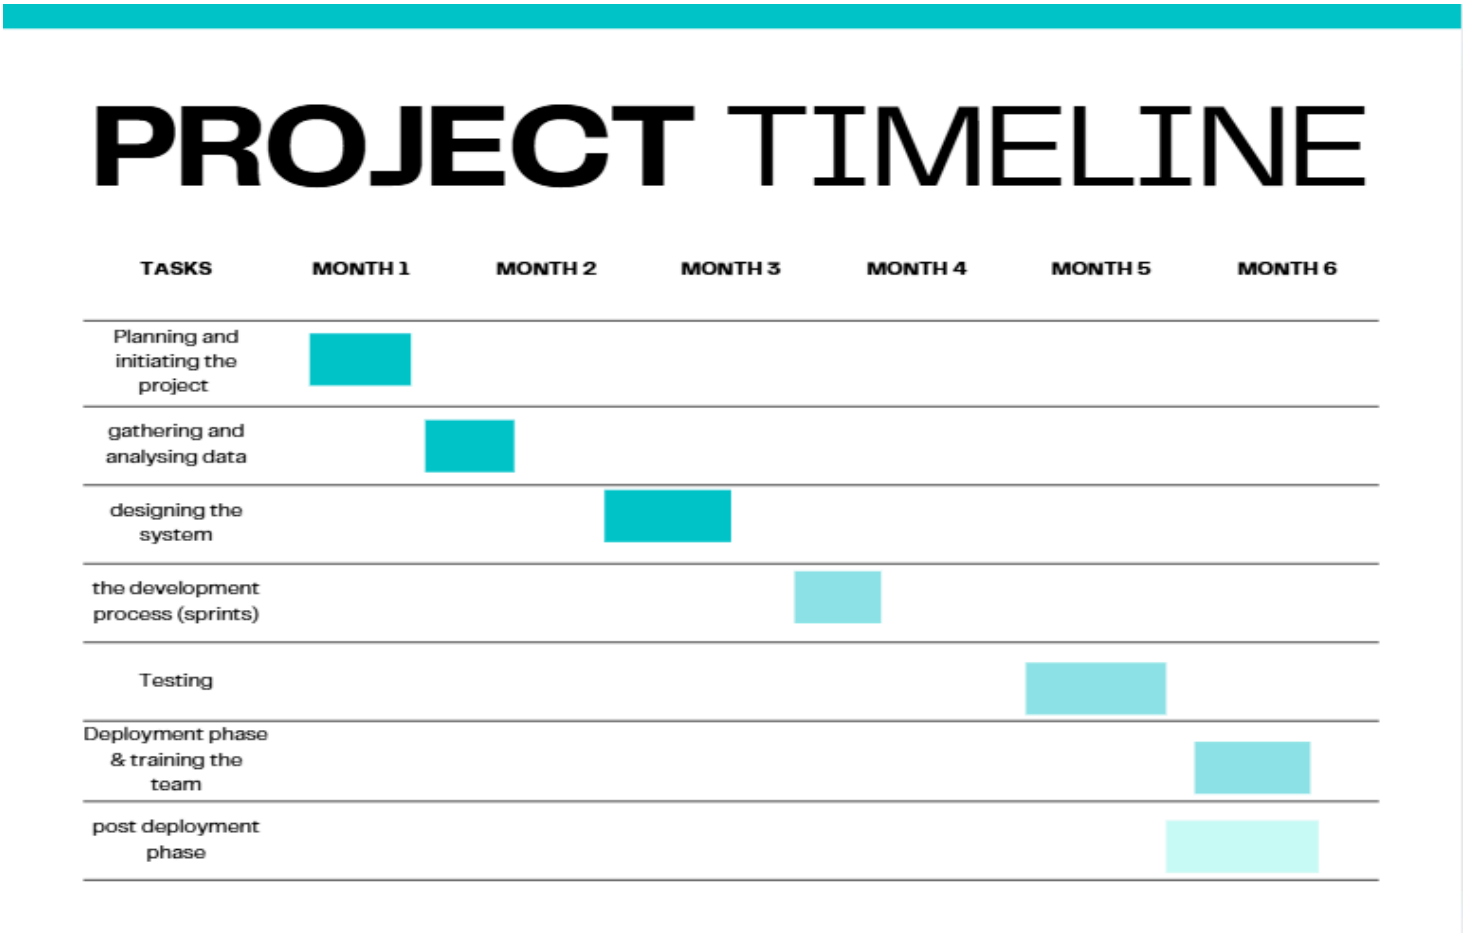

Appendix B – Risk Register

Risk	**Likelihood**	**Impact**
Data breach occurring during chatbot training due to how customer data gets handled	Medium	High
Failing to integrate the chatbot with website or mobile app leading to immediate stop	Medium	High
Inaccurate natural language processing responses that leads to poor user satisfaction	High	High
Incomplete training data which limits chatbot performance capabilities	High	Medium
Vendor delay or SaaS dependency issues that impacts schedule	Medium	Medium
Too many new ideas that causes delays leading to missing the deadline	High	Medium
Lack of proper skills in team members in AI and natural language processing technologies	Medium	Medium
Unexpected increase on the budget due to underestimating the cost of development and integration	Low	High
Cybersecurity threats	Medium	High
User adoption rates decrease if customers prefer human support.	Low	Medium

Appendix C – Progress Report Template

Appendix D – Burn Down Chart

Sprint Day	Ideal Work Remaining (Story Points)	Actual Work Remaining (Story Points)
2	40	40
4	38.0952381	38
6	36.19047619	35
8	34.28571429	32
10	32.38095238	28
12	30.47619048	24
14	28.57142857	19
16	26.66666667	14
18	24.76190476	10
21	22.85714286	5
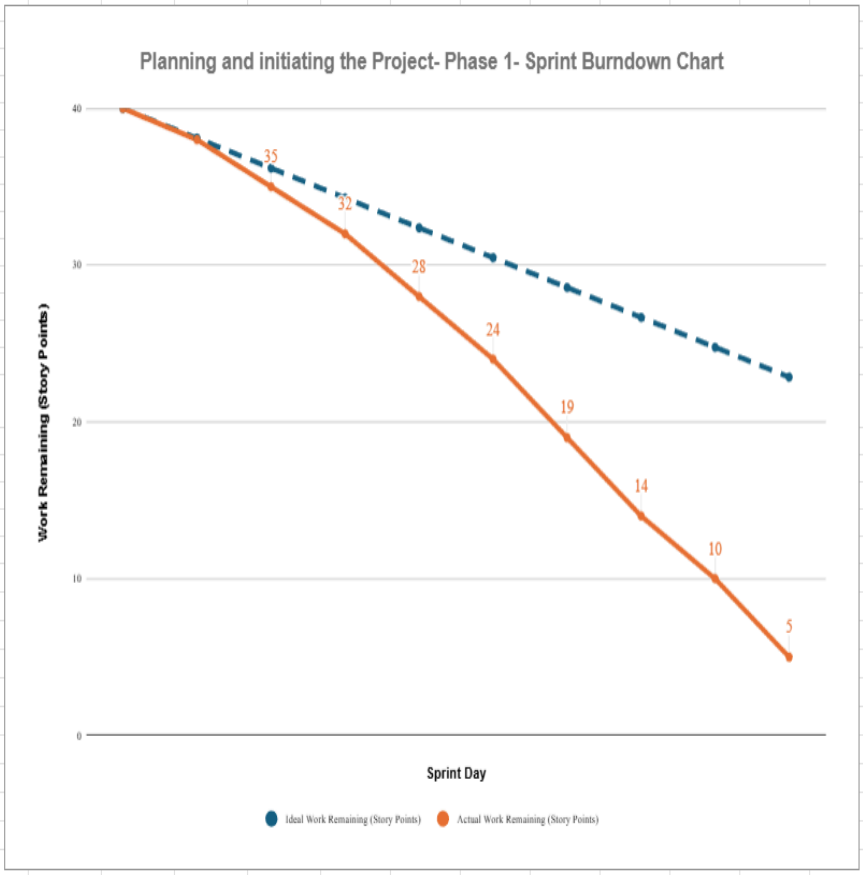
Total # Story Points	40
# Days in Sprint	21
Story Points to Complete per Day	1.904761905
